


Oulton-Stanish Centre Construction Update

December 16, 2024

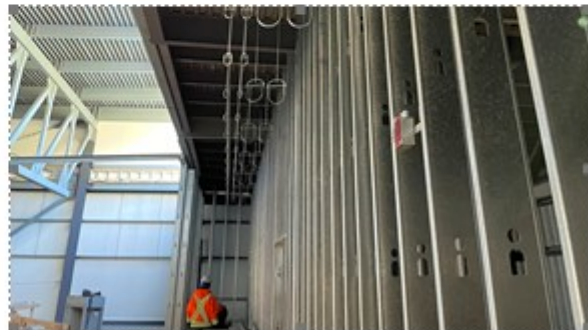

- Construction continues with exterior cladding and roof insulation installation as weather permits. We plan to begin the exterior brickwork at the north end in late December 2024.
- Precast bleachers are installed, which help the interior look more like a hockey arena! Rough-ins for mechanical, electrical, and fire suppression systems began recently, along with interior walls of steel stud and masonry block walls for the varsity locker rooms, reception area, and event rooms.
- Later this month, we'll begin connecting the OSC to the LeMarchant Place atrium for access to the new Dalhousie Physiotherapy Clinic on level 2. The atrium will be partially occupied, with access maintained at the LeMarchant St. and South St. entrances. Completion is scheduled for May 2025.
- Concrete for the ice rink is expected to be placed in late spring 2025.
- 95% of trade packages are finalized, with a few more to tender for next summer.
